PTC - Avenida D. Manuel I
Zona Industrial de Ovar
3880-109 OVAR

YAZAKI
PORTO TECHNICAL CENTRE

APPLICATOR VALIDATION REPORT

(Spec. YEL-RP-02-0004)

Applicator Serial Nº
S3141

TOOLS MANAGEMENT INFORMATION ---> TOOL Nº 72096619 SEQUENCE Nº 9

Terminal Nº	Rubber Seal	Applicator Type	Purchasing Order Nº	Project / Model
7209-6619-V2	*	**MSES1230-ZA**	**YSD-3500091458**	*







Anvil		
7209-6619MBAN/7209-6619MBAP		(N/N)
CW (c) 11,85	*CW (i)* 13,50	






Wire Crimper		
7209-6619MBW		(N)
CW 11,85		

Insulation Crimper		
7209-6619MBI		(N)
CW 13,50		

1 - VISUAL CHECK ITEMS

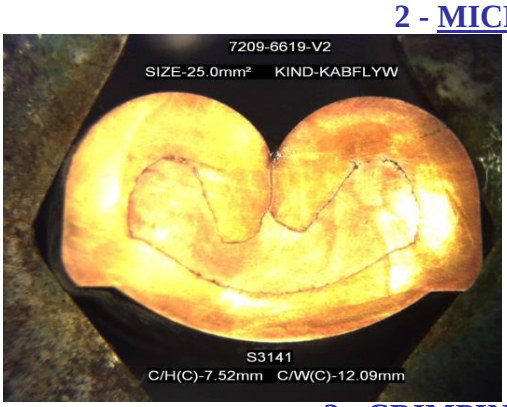
O - ok **X** - ng **NA** - not aplicable

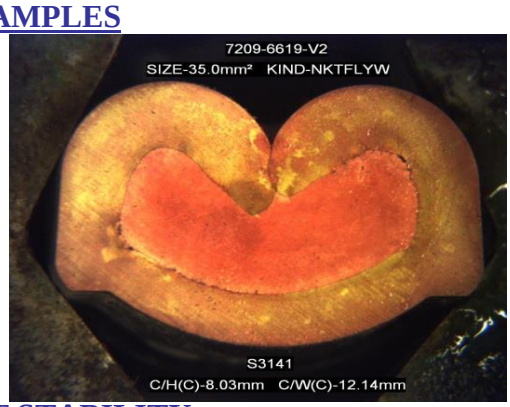
	The two sides of the insulation grips are in the correct position.	O
	Not found any Bell Mouth in the insulation area.	O
	The lance height and shape are not deformed.	NA
	Not found any burr in the cutting carrier.	NA
	Not found any crack in the terminal.	O
	The wire barrel is free from major burrs.	O

	The Bell Mouth is within the spec.**(*)**	O
	The dimension of the cutting carrier is within the spec.**(*)**	NA
	Bend up and Bend down are within the criteria**(*)**	O
	The exposed conductor is within the spec.(*)	O
	The terminal is not bent sideway, look-king from the top**(*)**	O
	The body of the terminal is not twisted**(*)**	O

LOWER WIRE KIND & SIZE	**UPPER** WIRE KIND & SIZE

2 - MICRO CUT SAMPLES





3 - CRIMPING HEIGHT STABILITY

	NOMINAL	AVERAGE	Cmk
mm	7,5	7,53	2,11
	+/-0,1		



	NOMINAL	AVERAGE	Cmk
mm	8	8,03	2,47
	+/-0,1		

REMARKS:

Aplicable wire range-25.0mm²~35.0mm².
Wire 25.0mm² C/W(I)-13.53mm
Wire 35.0mm² C/W(I)-13.68mm

EVALUATION DECISION

SUITABLE [X] FOR USE IN PRODUCTION
NOT SUITABLE [ ]

APPROVED (Section Chief) 3485	CHECKED (Operator) 8124	PREPARED (Operator) nº 2988
		
Date: 2019-fev-08	Date: 2019-fev-08	Date: 2019-fev-04

PORTO TECHNICAL CENTRE

APPLICATOR VALIDATION REPORT

Applicator Serial Nº
S3141

LOWER WIRE KIND & SIZE

Wire kind: KABFLYW

Wire size: 25 mm²

Nominal Cr. Height:	7,5	12,3	mm
+/-	0,1	0,1	mm

Sample number	Crimp height WIRE (mm)	Crimp height INSULATION (mm)
1	7,527	12,284
2	7,532	12,288
3	7,532	12,289
4	7,521	12,289
5	7,513	12,275
6	7,511	12,274
7	7,508	12,286
8	7,529	12,289
9	7,534	12,289
10	7,531	12,276
11	7,518	12,282
12	7,542	12,287
13	7,534	12,291
14	7,524	12,280
15	7,529	12,274
16	7,544	12,279
17	7,523	12,289
18	7,539	12,293
19	7,545	12,288
20	7,524	12,281
21	7,544	12,285
22	7,545	12,295
23	7,524	12,282
24	7,546	12,291
25	7,537	12,280
26	7,524	12,286
27	7,515	12,294
28	7,506	12,297
29	7,521	12,295
30	7,545	12,287
31	7,546	12,292
32	7,530	12,279
33	7,543	12,294
34	7,539	12,281
35	7,529	12,296
36	7,540	12,293
37	7,542	12,280
38	7,530	12,275
39	7,546	12,284
40	7,528	12,283
41	7,545	12,286
42	7,532	12,286
43	7,547	12,280
44	7,527	12,297
45	7,535	12,300
46	7,541	12,289
47	7,526	12,294
48	7,523	12,289
49	7,529	12,286
50	7,531	12,280
Average	7,53	12,29
Cmk	2,11	4,35

UPPER WIRE KIND & SIZE

Wire kind: NKTFLYW

Wire size: 35 mm²

Nominal Cr. Height:	8	13,1	mm
+/-	0,1	0,1	mm

Sample number	Crimp height WIRE (mm)	Crimp height INSULATION (mm)
1	8,026	13,116
2	8,024	13,107
3	8,026	13,104
4	8,049	13,098
5	8,041	13,110
6	8,031	13,113
7	8,048	13,113
8	8,036	13,096
9	8,052	13,096
10	8,036	13,111
11	8,041	13,118
12	8,056	13,116
13	8,034	13,119
14	8,030	13,104
15	8,031	13,097
16	8,042	13,098
17	8,025	13,111
18	8,019	13,104
19	8,025	13,117
20	8,033	13,098
21	8,044	13,094
22	8,029	13,109
23	8,047	13,117
24	8,040	13,124
25	8,030	13,125
26	8,043	13,124
27	8,039	13,106
28	8,036	13,122
29	8,029	13,110
30	8,029	13,104
31	8,045	13,120
32	8,036	13,110
33	8,050	13,120
34	8,032	13,125
35	8,029	13,109
36	8,036	13,118
37	8,029	13,103
38	8,030	13,107
39	8,023	13,105
40	8,024	13,107
41	8,030	13,107
42	8,021	13,105
43	8,038	13,116
44	8,038	13,111
45	8,022	13,098
46	8,029	13,117
47	8,033	13,103
48	8,021	13,122
49	8,036	13,118
50	8,042	13,099
Average	8,03	13,11
Cmk	2,47	3,43

Acceptance criteria: Cmk>= 2,0

END
