PTC - Avenida D. Manuel I
Zona Industrial de Ovar
3880-109 OVAR

YAZAKI
PORTO TECHNICAL CENTRE

APPLICATOR VALIDATION REPORT

(Spec. YEL-RP-02-0004)

Applicator Serial Nº
1907E059

TOOLS MANAGEMENT INFORMATION ---> TOOL Nº 7296-0099 * SEQUENCE Nº 9









Validation Terminal Nº	Accessory	Applicator Type	Purchasing Order Nº	Project / Model
7296-0099-02	**7158-3466-30**	**MYDR**	**YSD 4514078965**	**AIMLER TRUCK B**

Applicable Terminals for this Tool:

7296-0099-02	**7296-0099-06**			

Anvil		Wire Crimper		Insulation Crimper	
7296-0099XAD	(N)	7296-0099XW	(1)	7296-0099XID	(N)
CW (c) 1,80	*CW (i)* 3,30	*CW* 1,78		*CW* 3,30	


1 - VISUAL / MEASURED CHECK ITEMS


			Spec. (*)	Value (**)			
			O - ok **X** - ng **NA** - not aplicable				
	The two sides of the insulation grips are in the correct position.	**O**	0.00~0.15mm 0.15~0.35mm	0 0.32		The Bell Mouth is within the spec.**(*)**	**O**
	Not found any Bell Mouth in the insulation area.	**O**	0.00~0.30mm	0.29		The dimension of the cutting carrier is within the spec.**(*)**	**O**
	The lance height and shape are not deformed.	**O**	0.00~0.20mm 0.00~0.20mm	-- 0.10		Bend up and Bend down are within the criteria**(*)**	**O**
	Not found any burr in the cutting carrier.	**O**	0.10~0.40mm	0.36		The exposed conductor is within the spec.(*)	**O**
	Not found any crack in the terminal.	**O**	5º	1.6		The terminal is not bent sideway, look-king from the top**(*)**	**O**
	The wire barrel is free from major burrs.	**O**	0.00~0.30mm	0.06		The body of the terminal is not twisted**(*)**	**O**

(*) - Specified on Crimping Spec. **(**)** - Measured Value(From Lower Wire Kind&Size Sample)

LOWER WIRE KIND & SIZE	**UPPER** WIRE KIND & SIZE

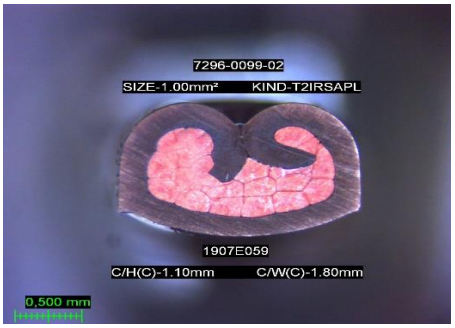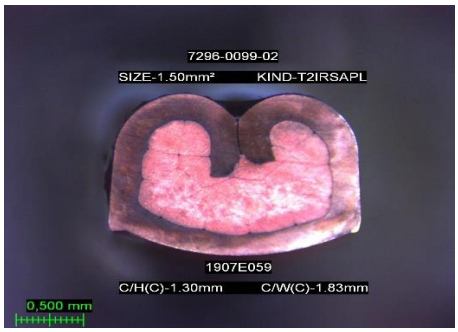2 - MICRO CUT SAMPLES





3 - CRIMPING HEIGHT STABILITY

	NOMINAL	AVERAGE	Cmk
mm	1,1	1,10	3,12
	+/-0.05		

	NOMINAL	AVERAGE	Cmk
mm	1,31	1,31	3,49
	+/-0.05		

REMARKS:

Aplicable wire range 1.00mm²~1.50mm²
Wire size 1.00mm² C/W(I)-3.32mm
Wire size 1.50mm² C/W(I)-3.40mm

EVALUATION DECISION

SUITABLE [X]
NOT SUITABLE [ ]
FOR USE IN PRODUCTION

APPROVED (Section Chief) 3485	CHECKED (Operator) 44	PREPARED (Operator) nº 19147
Date: 2024/jul/08	Date: 2024/jun/25	Date: 2024/jun/21

YAZAKI
PORTO TECHNICAL CENTRE

APPLICATOR VALIDATION REPORT

Applicator Serial Nº
1907E059

LOWER WIRE KIND & SIZE

Wire kind: T2IRSAPL

Wire size: 1 mm²

Nominal Cr. Height:	1,1	3,3	mm
+/-	0,05	0,1	mm

Sample number	Crimp height WIRE (mm)	Crimp height INSULATION (mm)
1	1,104	3,301
2	1,104	3,305
3	1,109	3,305
4	1,107	3,308
5	1,104	3,306
6	1,104	3,305
7	1,101	3,301
8	1,101	3,300
9	1,100	3,298
10	1,099	3,296
11	1,096	3,295
12	1,094	3,297
13	1,094	3,306
14	1,099	3,309
15	1,101	3,309
16	1,103	3,309
17	1,107	3,313
18	1,110	3,299
19	1,111	3,298
20	1,111	3,298
21	1,113	3,302
22	1,097	3,304
23	1,097	3,305
24	1,094	3,308
25	1,092	3,311
26	1,093	3,314
27	1,098	3,314
28	1,098	3,309
29	1,099	3,306
30	1,102	3,303
31	1,104	3,301
32	1,105	3,297
33	1,106	3,297
34	1,108	3,303
35	1,108	3,304
36	1,101	3,307
37	1,099	3,308
38	1,095	3,308
39	1,095	3,310
40	1,095	3,311
41	1,094	3,303
42	1,097	3,296
43	1,099	3,295
44	1,100	3,292
45	1,101	3,292
46	1,101	3,301
47	1,102	3,304
48	1,103	3,306
49	1,104	3,307
50	1,104	3,310
Average	1,10	3,30
Cmk	3,12	5,68

UPPER WIRE KIND & SIZE

Wire kind: T2IRSAPL

Wire size: 1,5 mm²

Nominal Cr. Height:	1,31	3,6	mm
+/-	0,05	0,1	mm


Sample number	Crimp height WIRE (mm)	Crimp height INSULATION (mm)
1	1,316	3,605
2	1,311	3,598
3	1,310	3,597
4	1,307	3,593
5	1,303	3,601
6	1,301	3,604
7	1,304	3,608
8	1,309	3,612
9	1,310	3,614
10	1,312	3,606
11	1,314	3,599
12	1,315	3,597
13	1,317	3,596
14	1,308	3,603
15	1,304	3,604
16	1,301	3,606
17	1,300	3,608
18	1,299	3,610
19	1,302	3,606
20	1,304	3,602
21	1,310	3,599
22	1,312	3,595
23	1,313	3,593
24	1,307	3,602
25	1,305	3,605
26	1,303	3,609
27	1,308	3,612
28	1,310	3,613
29	1,312	3,612
30	1,312	3,608
31	1,307	3,606
32	1,305	3,606
33	1,303	3,602
34	1,305	3,599
35	1,311	3,599
36	1,314	3,606
37	1,315	3,608
38	1,313	3,610
39	1,308	3,600
40	1,306	3,596
41	1,311	3,596
42	1,314	3,590
43	1,315	3,605
44	1,316	3,605
45	1,311	3,587
46	1,310	3,594
47	1,308	3,598
48	1,308	3,599
49	1,312	3,601
50	1,312	3,603
Average	1,31	3,60
Cmk	3,49	5,22

Acceptance criteria: Cmk>= 2,0

END

04 APPLICATOR CONSUMABLE PARTS LIST ／ 04 アプリケーター 消耗部品表

PRODUCT No. 製品番号	C0100-5765	TERMINAL No. 端子品番	7296-0099 DD
共通品番	– – – – – – – –		

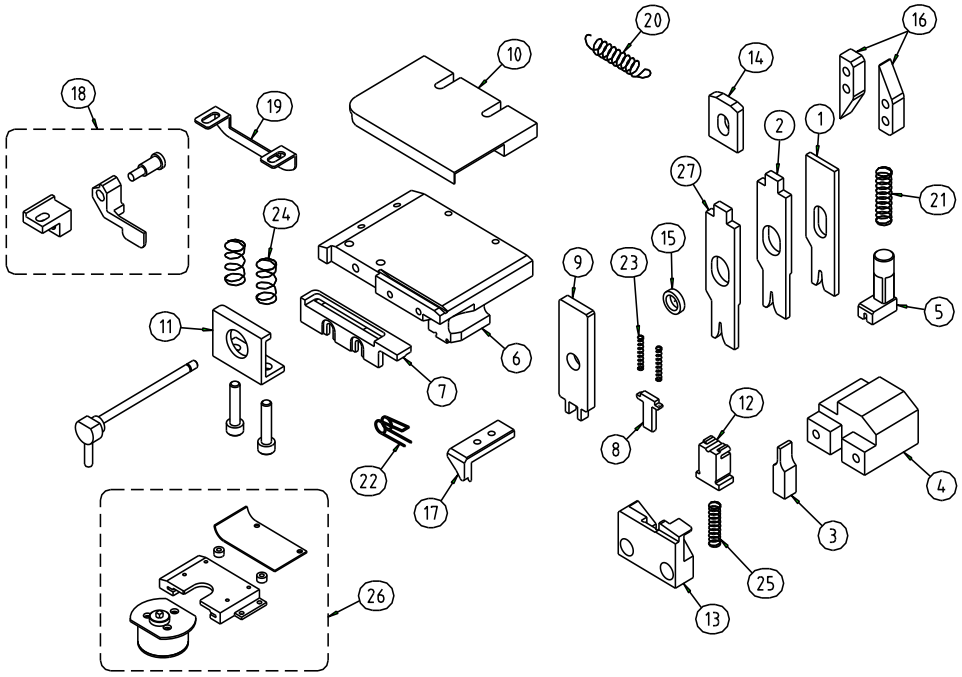

No,	PARTS No, 部品番号	DRW No, 図番	PARTS NAME 部品名称	No,	PARTS No, 部品番号	DRW No, 図番	PARTS NAME 部品名称
1	7296-0099XW		WIRE CRIMPER ワイヤークリンパー	17	48A47013	-001	FEEDING CLAW 送り爪
2	7296-0099XID		INSULATION CRIMPER インシュレーションクリンパー	18	48A19100	-005	WIRE STOPPER Assy 電線ストッパー アッシー
3	7296-0099XAD		ANVIL アンビル	19	48A19047	-001	TERMINAL SCRAPER 端子掻き落とし
4	7296-0099XJE		ANVIL HOLDER アンビルホルダー	20	48A47031		RETURN SPRING 戻しスプリング
5	7296-0099XYY		SUPPORTING STOPPER サポーティングストッパー	21	48A47032	-002	SUPPORTING STOPPER SPRING サポーティングストッパースプリング
6	7296-0099XYB		BASE ベース	22	48A19017	-003	FEEDING CLAW SPRING 送り爪スプリング
7	7296-0099XYH		TERMINAL GUIDE PLATE B ターミナルガイドプレートB	23	48A19023	-002	WIRE HOLDER SPRING 電線押さえスプリング
8	48A47016	-002	WIRE HOLDER 電線押さえ	24	48A19074		TERMINAL HOLDER SPRING ターミナル押さえスプリング
9	48A47017	-002	CUTTING PUNCH & WIRE HOLDER 切断ポンチ兼電線押さえホルダー	25	48A19050		SHEARBLADE SPRING シャーブレードスプリング
10	48A47020	-A04	TERMINAL GUIDE PLATE A ターミナルガイドプレートA	26	48A19999		TERMINAL OIL UNIT ターミナル塗油ユニット
11	48A47022	-001	TERMINAL HOLDER ターミナル押さえ		7296-0099XKP		BRACKET ブラケット
12	48A19049	-002	SHEARBLADE シャーブレード	27	~~7296-0099XQ~~		~~STABILIZER CRIMPER スタビライザークリンパー~~
13	48A47025	-003	OUTER SHEARBLADE アウターシャーブレード	〈OPTION オプション〉			
14	48A19007	-018	INSULATION ADJUSTING PIECE インシュレーション調整コマ	13	48A47025	-101	OUTER SHEARBLADE アウターシャーブレード
15	48A19019	-027	BUSH ブッシュ	14	48A47042	-002	INSULATION ADJUSTING PIECE(MECAL) インシュレーション調整コマ(メカル)
16	48A47014	-003	FEEDING CAM 送りカム				

MARK 記号	DATE 日付	REVISION RECORD 改訂記録	No. 番号	CHECKED 点検

APPRICATION POST 申請部署		
YWTS		
DESIGNED DATE 設計日		
01-10-2013		
APPROVED 承認	DESIGNED 設計	ISSUED 発行
T,Maki	C.Almeida	
01-10-2013	01-10-2013	
