PTC - Avenida D. Manuel I
Zona Industrial de Ovar
3880-109 OVAR

YAZAKI
PORTO TECHNICAL CENTRE



# APPLICATOR VALIDATION REPORT

**(Spec. YEL-RP-02-0004)**

| Applicator Serial Nº |
|---|
| S3085 |

***TOOLS MANAGEMENT INFORMATION ---> TOOL Nº 72096620 SEQUENCE Nº 9***






| Terminal Nº | Rubber Seal | Applicator Type | Purchasing Order Nº | Project / Model |
|---|---|---|---|---|
| **7209-6620-V2** | * | **MSES1230-Z** | **YSD-3500091458** | * |

| Anvil | | |
|---|---|---|
| 7209-6620MBAN/7209-6620MBAP | | (N/N) |
| *CW (c)* 11,85 | *CW (i)* 13,50 | |




| Wire Crimper | |
|---|---|
| 7209-6620MBW | (N) |
| *CW* 11,85 | |

| Insulation Crimper | |
|---|---|
| 72096620MBI | (N) |
| *CW* 13,50 | |

## 1 - VISUAL CHECK ITEMS

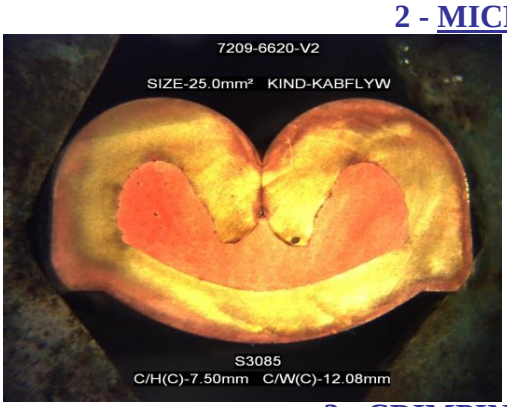
| | | |
|---|---|---|
|  | The two sides of the insulation grips are in the correct position. | O |
|  | Not found any Bell Mouth in the insulation area. | O |
|  | The lance height and shape are not deformed. | NA |
|  | Not found any burr in the cutting carrier. | NA |
|  | Not found any crack in the terminal. | O |
|  | The wire barrel is free from major burrs. | O |

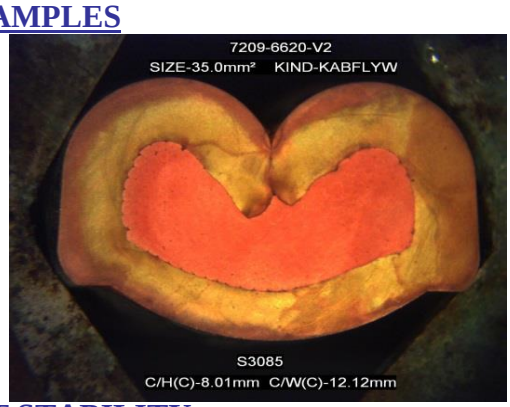
**O** - ok **X** - ng **NA** - not aplicable

| | | |
|---|---|---|
|  | The Bell Mouth is within the spec.**(*)** | O |
|  | The dimension of the cutting carrier is within the spec.**(*)** | NA |
|  | Bend up and Bend down are within the criteria**(*)** | O |
|  | The exposed conductor is within the spec.(*) | O |
|  | The terminal is not bent sideway, look-king from the top**(*)** | O |
|  | The body of the terminal is not twisted**(*)** | O |

| **LOWER** WIRE KIND & SIZE | **UPPER** WIRE KIND & SIZE |
|---|---|

## 2 - MICRO CUT SAMPLES




## 3 - CRIMPING HEIGHT STABILITY

| | NOMINAL | AVERAGE | Cmk |
|---|---|---|---|
| mm | 7,5 | 7,51 | 3,04 |
| | **+/-0,1** | | |

| | NOMINAL | AVERAGE | Cmk |
|---|---|---|---|
| mm | 8 | 8,01 | 3,31 |
| | **+/-0,1** | | |

**REMARKS:**

Aplicable wire range-25.0mm²~35.0mm².
Wire 25.0mm² C/W(I)-13.62mm
Wire 35.0mm² C/W(I)-13.70mm

**EVALUATION DECISION**

SUITABLE [X]
NOT SUITABLE [ ]
FOR USE IN PRODUCTION

| APPROVED (Section Chief) 3485 | CHECKED (Operator) 44 | PREPARED (Operator) nº 5061 |
|---|---|---|
| | | |
| Date: 2018-dez-04 | Date: 2018-nov-27 | Date: 2018-nov-27 |

**PORTO TECHNICAL CENTRE**

# APPLICATOR VALIDATION REPORT

| Applicator Serial Nº |
|---|
| S3085 |

## LOWER WIRE KIND & SIZE

Wire kind: KABFLYW

Wire size: 25 mm²

| | | | |
|---|---|---|---|
| Nominal Cr. Height: | 7,5 | 12,4 | mm |
| +/- | 0,1 | 0,1 | mm |

| Sample number | Crimp height WIRE (mm) | Crimp height INSULATION (mm) |
|---|---|---|
| 1 | 7,516 | 12,402 |
| 2 | 7,522 | 12,412 |
| 3 | 7,507 | 12,404 |
| 4 | 7,516 | 12,401 |
| 5 | 7,508 | 12,415 |
| 6 | 7,524 | 12,411 |
| 7 | 7,513 | 12,400 |
| 8 | 7,521 | 12,413 |
| 9 | 7,513 | 12,402 |
| 10 | 7,521 | 12,407 |
| 11 | 7,518 | 12,415 |
| 12 | 7,507 | 12,418 |
| 13 | 7,505 | 12,407 |
| 14 | 7,504 | 12,419 |
| 15 | 7,513 | 12,403 |
| 16 | 7,517 | 12,419 |
| 17 | 7,516 | 12,413 |
| 18 | 7,518 | 12,410 |
| 19 | 7,521 | 12,408 |
| 20 | 7,517 | 12,406 |
| 21 | 7,521 | 12,401 |
| 22 | 7,527 | 12,413 |
| 23 | 7,514 | 12,405 |
| 24 | 7,504 | 12,399 |
| 25 | 7,509 | 12,400 |
| 26 | 7,498 | 12,398 |
| 27 | 7,488 | 12,410 |
| 28 | 7,480 | 12,397 |
| 29 | 7,500 | 12,405 |
| 30 | 7,486 | 12,395 |
| 31 | 7,503 | 12,403 |
| 32 | 7,497 | 12,396 |
| 33 | 7,519 | 12,401 |
| 34 | 7,515 | 12,407 |
| 35 | 7,509 | 12,394 |
| 36 | 7,518 | 12,401 |
| 37 | 7,519 | 12,393 |
| 38 | 7,503 | 12,404 |
| 39 | 7,516 | 12,389 |
| 40 | 7,517 | 12,403 |
| 41 | 7,504 | 12,390 |
| 42 | 7,501 | 12,402 |
| 43 | 7,512 | 12,391 |
| 44 | 7,505 | 12,399 |
| 45 | 7,503 | 12,396 |
| 46 | 7,513 | 12,392 |
| 47 | 7,504 | 12,396 |
| 48 | 7,514 | 12,392 |
| 49 | 7,503 | 12,398 |
| 50 | 7,514 | 12,399 |
| Average | 7,51 | 12,40 |
| Cmk | 3,04 | 4,15 |

## UPPER WIRE KIND & SIZE

Wire kind: KABFLYW

Wire size: 35 mm²

| | | | |
|---|---|---|---|
| Nominal Cr. Height: | 8 | 13,1 | mm |
| +/- | 0,1 | 0,1 | mm |

| Sample number | Crimp height WIRE (mm) | Crimp height INSULATION (mm) |
|---|---|---|
| 1 | 8,010 | 13,112 |
| 2 | 8,013 | 13,119 |
| 3 | 8,004 | 13,114 |
| 4 | 8,016 | 13,120 |
| 5 | 8,013 | 13,107 |
| 6 | 7,998 | 13,113 |
| 7 | 8,004 | 13,119 |
| 8 | 7,998 | 13,112 |
| 9 | 8,000 | 13,110 |
| 10 | 8,003 | 13,115 |
| 11 | 8,000 | 13,116 |
| 12 | 8,011 | 13,112 |
| 13 | 8,014 | 13,107 |
| 14 | 8,003 | 13,097 |
| 15 | 8,007 | 13,096 |
| 16 | 8,012 | 13,106 |
| 17 | 8,002 | 13,104 |
| 18 | 8,011 | 13,101 |
| 19 | 7,996 | 13,096 |
| 20 | 8,007 | 13,104 |
| 21 | 8,001 | 13,098 |
| 22 | 8,016 | 13,093 |
| 23 | 8,000 | 13,099 |
| 24 | 8,026 | 13,103 |
| 25 | 8,025 | 13,095 |
| 26 | 8,004 | 13,102 |
| 27 | 8,023 | 13,102 |
| 28 | 8,004 | 13,097 |
| 29 | 8,001 | 13,105 |
| 30 | 8,013 | 13,107 |
| 31 | 8,005 | 13,099 |
| 32 | 8,003 | 13,102 |
| 33 | 8,014 | 13,105 |
| 34 | 8,020 | 13,101 |
| 35 | 8,026 | 13,096 |
| 36 | 8,006 | 13,103 |
| 37 | 8,017 | 13,110 |
| 38 | 8,025 | 13,100 |
| 39 | 8,006 | 13,094 |
| 40 | 8,026 | 13,093 |
| 41 | 8,026 | 13,100 |
| 42 | 8,005 | 13,106 |
| 43 | 8,014 | 13,096 |
| 44 | 8,005 | 13,102 |
| 45 | 8,001 | 13,094 |
| 46 | 8,024 | 13,101 |
| 47 | 8,022 | 13,103 |
| 48 | 8,010 | 13,109 |
| 49 | 8,000 | 13,096 |
| 50 | 7,997 | 13,101 |
| Average | 8,01 | 13,10 |
| Cmk | 3,31 | 4,41 |

**END**
